

Cemex Newsletter

Willington, Quarry Extension – April 2025

Following the grant of planning permissions, pre-development works for the quarry extension are planned to commence during April. These will commence with the construction of the temporary bridge over the River Dove, which should take approximately 4 weeks. Once the bridge is in place the haul road will be constructed from the bridge to the quarry, this will take approximately 2 weeks. During this period, you may see pre-development geoarchaeology borehole surveys taking place in the field opposite Newton Solney, during April.


Regular updates will be provided, please see below the initial operational timetable.

Bridge Installation

- Start: Mid-April 2025
- End: Mid-May 2025


Haul Road (from bridge to quarry) construction

- Start: Mid-May 2025
- End: Early June 2025

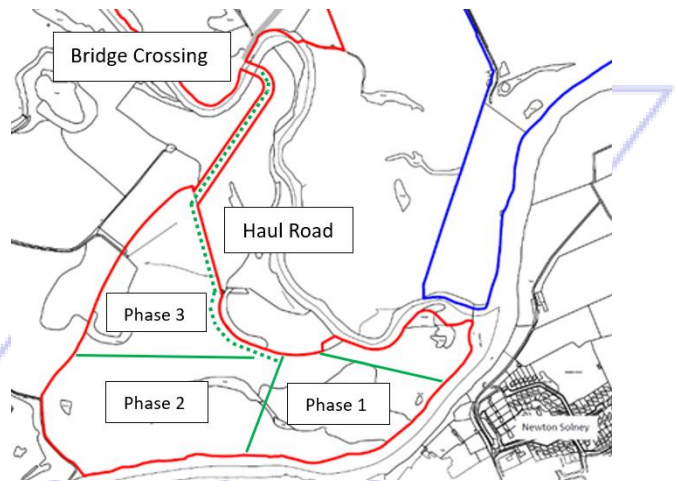

Soil Strip – Phase 1

- Soil strip to create screening bund between Phase 1 and the River Trent**
 - Start: Early June 2025
 - End: Mid-June 2025
- Remainder of soil strip and place into temporary storage mounds**
 - Start: Mid-June 2025
 - End: Mid July 2025

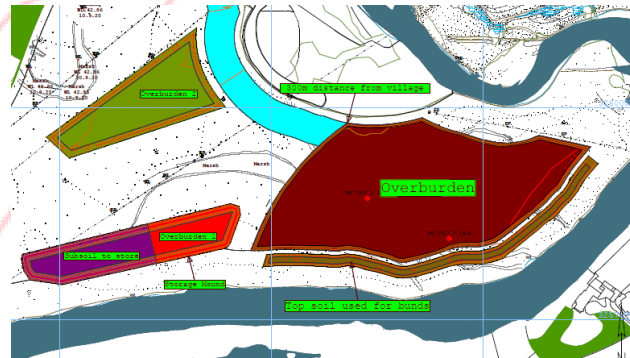

If you have any queries, please contact Newton Solney Parish Council, who will redirect your query to Cemex.

